ID	Name	Dur
071220		199d
1	Site Set Up	2d
2	Demolition	15d
3	Strip roof to West Wing	5d
4	Strip stone to west wing	5d
5	Demolish west wing	4d
6	Sub Structure W/W	11d
7	RLD	1d
8	Foundations	3d
9	Footings	3d
10	Oversite	3d
11	Drainage	1d
12	Sub Structure E/W	6d
13	RLD	1d
14	Foundations	2d
15	Footings	1d
16	Oversite	2d
17	Super Structure	149d
18	B/W to First Lift	7d
19	S/W to First Lift	15d
20	B/W to Joist	5d
21	S/W to Joist	15d
22	Install Joists & Steels	5d
23	B/W to 3rd lift	5d
24	S/W to 3rd Lift	10d
25	B/W to Plate E/W	5d
26	S/W to plate E/W	10d
27	Chimney to W/W	5d
28	Chimney to E/W	10d
29	Structural Roofing	20d
30	Gable to West wing	11d
31	Roof Covering W/W	20d
32	Strip roof E/W	5d
33	Roof Covering E/W	20d
34	West Wing Internal	52d
35	First Fix	10d
36	Carpentry	10d
37	Mechanical	5d
38	Electrical	5d
39	Plaster & Screed	13d
40	Second Fix	15d
41	Carpentry	15d
42	Mechanical	5d
43	Electrical	5d
44	Floor & Wall Finishes	10d
45	Decorations	20d
46	East Wing Internal	160d
47	Remove Existing Stairs	1d
48	Masonry Alterations	10d
49	Substructure to Hall	6d
50	Work to Fireplaces	10d
51	Floor Joists to Landing	2d
52	First Fix	10d
53	Carpentry	10d
54	Mechanical	5d
55	Electrical	5d
56	Plaster & Screed	10d
57	Second Fix	25d
58	Carpentry	10d
59	Mechanical	5d
60	Electrical	5d
61	Decorations to E/W	15d
62	Remove end wall to bed	5d
63	Complete 1st fix bed1 &	5d
64	Plaster/Screed Bed 1 &	5d
65	Complete 2nd Fix Bed1	10d
66	Floor & Wall Finishes	15d
67	Decorations Bed 1 &	15d
68	External Works	20d
69	Completion	0d

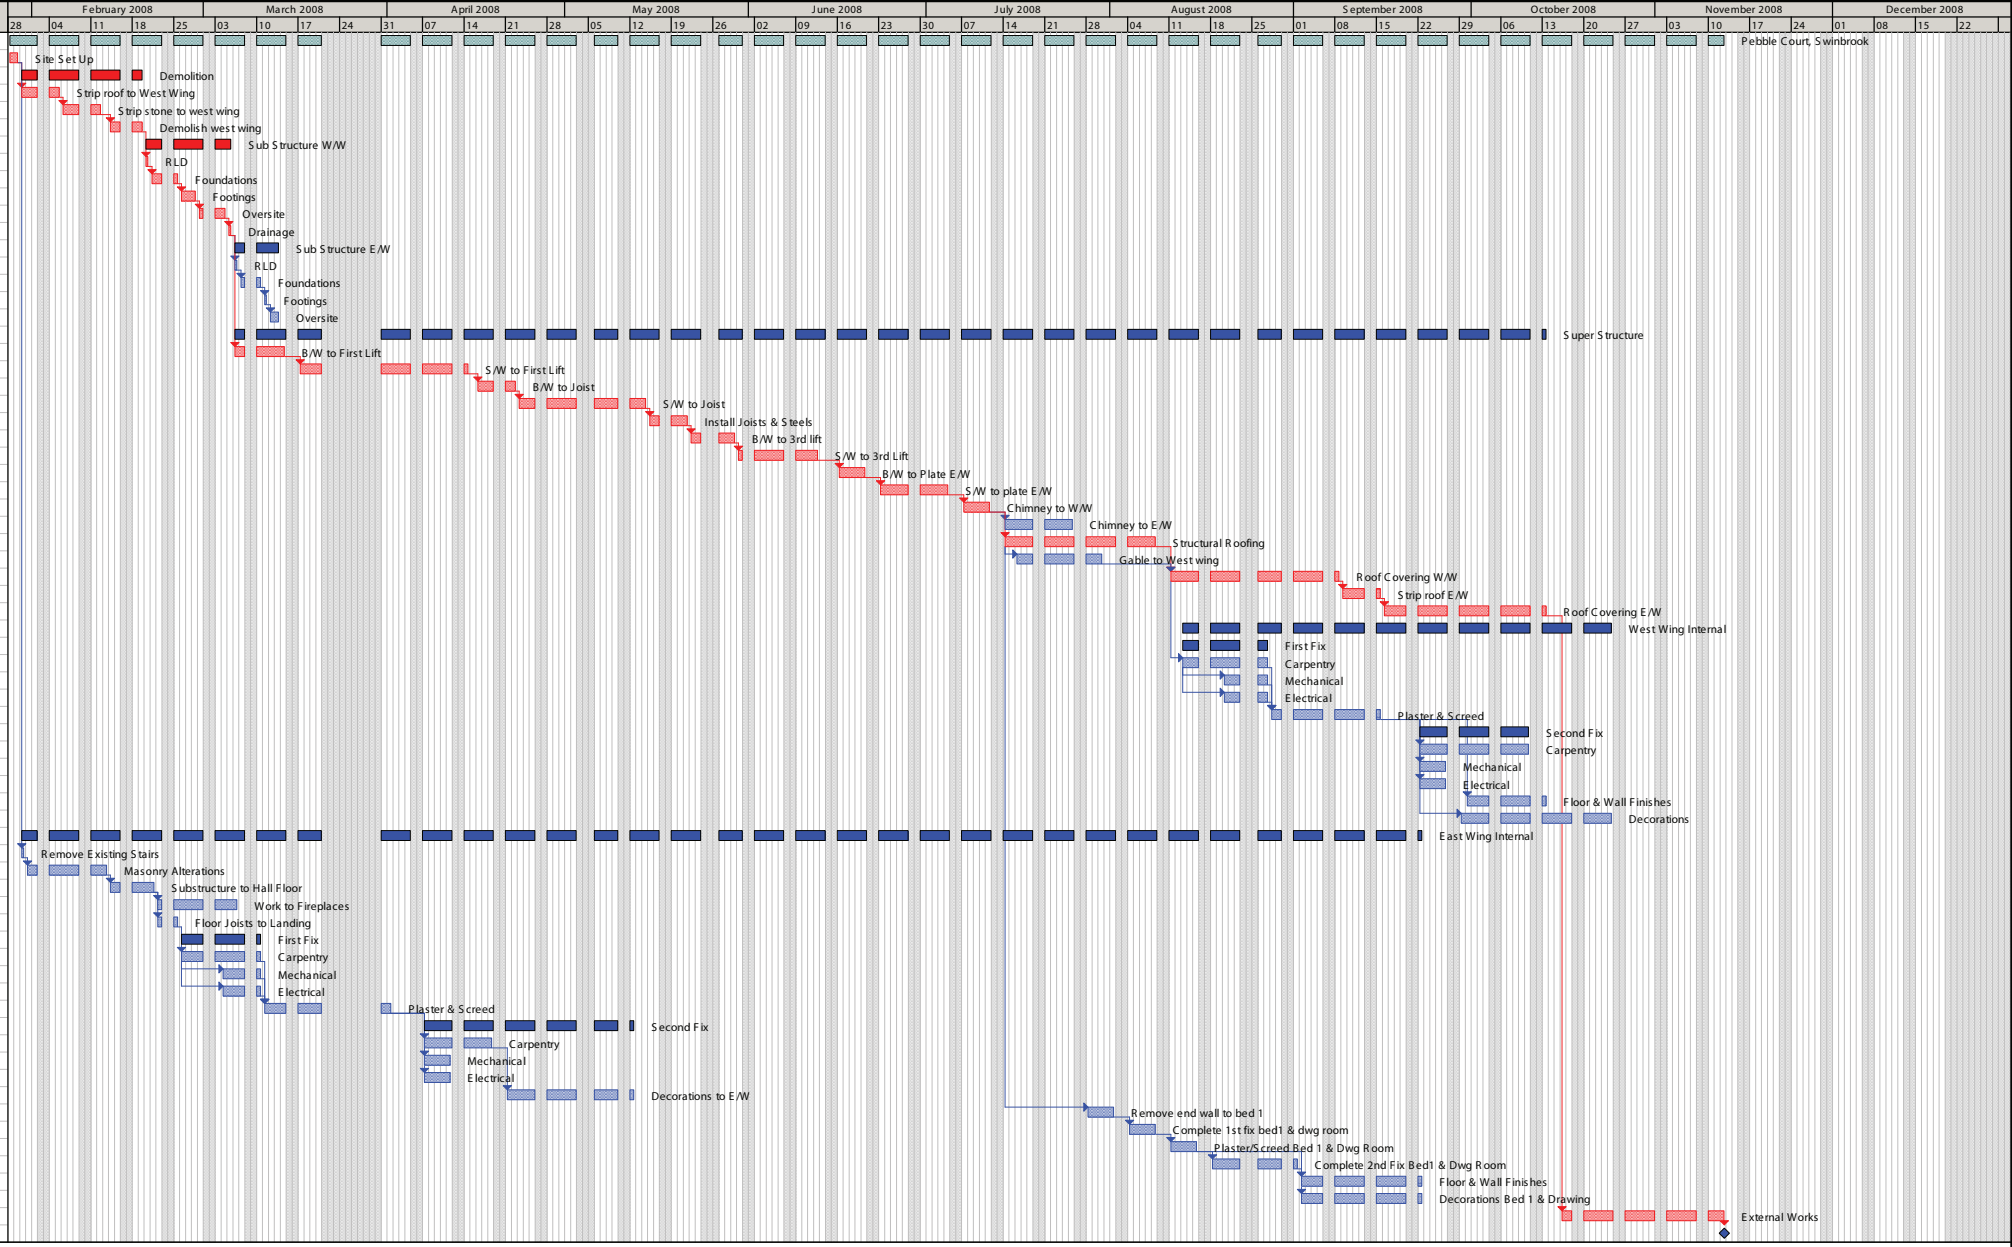

Detail Normal | Summary Normal | Detail Critical | Summary Critical | Detail Super-Critical | Summary Super-Critical | Baseline1 | Project | Percent Complete | Milestone | Baseline1 Milestone
